



Certificate of Test &/Or Examination

Issued to

Metcalf Crane Services Pty Ltd
UNIT 84

Certificate Number

BEL71453

Date of Test / Inspection

26 Nov 2025

Invoice Number

41263

Customer Reference

PO002168

Location

Unit 84

Qty Tested	Customer I/D	S/N	Description	Effective Length	WLL	Proof Load
1		CR84	14MM X 110M CRANE ROPE C/W Machine Spliced Thimble Eye One End Copper Stopper Other End CONST: 35/7 GRADE: 1960 LAY: RHLL FINISH: Galvanised MANF: Terex	110M		

Test/Inspection Method:

In Accordance With: AS2759

Result:

PASSED

Overall Comments

On release all items tested/inspected were found to be free from any deleterious permanent set or defects that could be detected by visual inspection.

Declaration


The above detailed items comply with the appropriate clauses of AS2759

Examined by

Zane Booth-Bruscino

Approved Signatory

Craig Bozelle

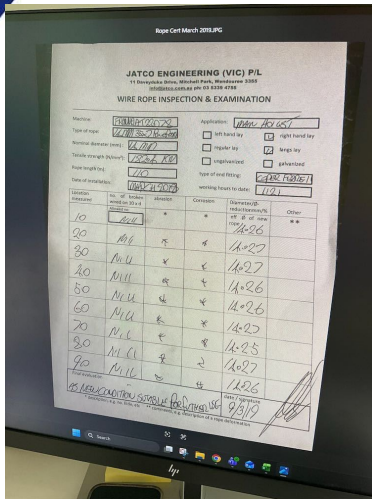

IMG_1764128288519
