



Cantech Engineering & Consulting LTD
5160 Skyline Way NE
Calgary, AB. T2E 6V1
(403) 456-4594

MEZEI INSPECTION LTD.
4917 Beckett Road
Drayton Valley, AB. T7A 1E6
(780) 515-0630

FILE NO.: MIL - 25-0089


ENGINEERING CERTIFICATION

EQUIPMENT: PICKER TRUCK
MAKE: FASSI
MODEL: F65A.0.24
SERIAL: 0609-1042
OWNER: Bailey's Welding and Construction Inc
OWNER UNIT #: 950
CERTIFIED DATE: November 13, 2025

Based on the Equipment Inspection Report (#25-0089) submitted by Mezei Inspection Ltd. On 13 November 2025, it has been determined that there were no indications of cracked or damaged welds on the equipment and it has been found to be suitable for service.

I certify that all welds that have been examined by Mezei Inspection Ltd. conform to industry standards. This certification is valid for a maximum period of one year from the inspection date. The unit is to be re-inspected if it sustains damage to a structural area.

CANTECH ENGINEERING & CONSULTING LTD.





Cantech Engineering & Consulting LTD
5160 Skyline Way NE
Calgary, AB. T2E 6V1
(403) 456-4594

MEZEI INSPECTION LTD.
4917 Beckett Road
Drayton Valley, AB. T7A 1E6
(780) 515-0630

Report: 25-0089

EQUIPMENT INSPECTION REPORT

Client:	Bailey's Welding & Construction Inc	Date:	November 13, 2025
Equipment:	Picker Truck	Attachment:	
Unit:	950	Make:	
Make:	FASSI	Model:	
Model:	F65.0.24	S/N:	
S/N:	0609-1042	Insp Code:	OHSA & CSA Z150-20 & W59-2024
Location:	Drayton Valley, AB		

MAGNITIZATION

Method: Yoke S.N: MP5791
Current: Alternating (AC)
Field: Continuous

PARTICLE


Medium: Magnaflux
Type: Grey Powder
Application: Bottle Puffer

PROCEDURE

Technique: MT-EY1
Surface Cond.: In Service
Demagnification: ASME V Art.7
Post Cleaning: Ardrex Cleaner

Visual & Magnetic Particle Inspection to ASTM E709 were performed on the above described equipment with the following results.

A full-length inspection was conducted on the picker and outriggers. No Indications were found at the time of final inspection.

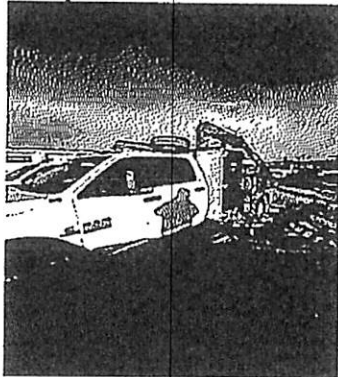

☐ Repairs Required

☐ Repairs Complete

☒ Sticker Applied.

INSPECTOR: Eric Mezei

SIGNATURE: Eric Mezei

INSPECTORS STAMP

Eric Mezei
CGSB Level 2 RT MT PT
SNT Level II RT MT PT
Reg# 12893



Cantech Engineering & Consulting LTD
5160 Skyline Way NE
Calgary, AB. T2E 6V1
(403) 456-4594

MEZEI INSPECTION LTD.
4917 Beckett Road
Drayton Valley, AB. T7A 1E6
(780) 515-0630

Report: 25-0089

EQUIPMENT INSPECTION CHECK LIST

COMPONENTS	DEFECTS	OK	DEFECT IDENTIFICATIONS
Picker Model, S/N on structure	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Load Rating Chart	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Load Indicator Device (LID)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Boom Angle Indicator	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Boom Length Indicator	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Outrigger Vertical Rams	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Outrigger Boxes	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Outrigger Extensions	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Outrigger Pads	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Outrigger Welds	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Main Boom	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1st Extension	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2nd Extension	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3rd Extension	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4th Extension	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Boom Rest Hook	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Boom Section Wear Pads	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Boom Head Sheaves	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Rotating Frame Welds	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Structure Members between outrigger boxes	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Deck	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Check holding nuts and bolts	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Other:	<input type="checkbox"/>	<input type="checkbox"/>	
Other:	<input type="checkbox"/>	<input type="checkbox"/>	
Other:	<input type="checkbox"/>	<input type="checkbox"/>	

