


F24-39  
BLUE-MAR

 <b>Icon Energy Services Ltd.</b> 268 Clearview Drive Red Deer County, Alberta, T4E 0A1 Phone: (403) 340-2225 Email: ndt@iconenergyservices.ca	<h2 style="margin:0;">NDT REPORT</h2> No. <span style="font-size: 1.2em;">DS-0958</span>																																																						
<table border="1" style="width:100%; border-collapse: collapse;"> <tr><td>Customer</td><td><b>TEKH GROUP INC.</b></td></tr> <tr><td>Branch</td><td>-</td></tr> <tr><td>Equipment Type</td><td>Side Boom</td></tr> <tr><td>Make</td><td>Caterpillar</td></tr> <tr><td>Model</td><td>D6C</td></tr> <tr><td>Capacity</td><td>Refer to OEM Capacity</td></tr> <tr><td>Size</td><td>-</td></tr> <tr><td>Other</td><td>-</td></tr> <tr><td>OEM S/N</td><td>90B596</td></tr> <tr><td>Customer ID</td><td>-</td></tr> <tr><td>Rig/Unit:</td><td>72-634</td></tr> </table>	Customer	<b>TEKH GROUP INC.</b>	Branch	-	Equipment Type	Side Boom	Make	Caterpillar	Model	D6C	Capacity	Refer to OEM Capacity	Size	-	Other	-	OEM S/N	90B596	Customer ID	-	Rig/Unit:	72-634	<table border="1" style="width:100%; border-collapse: collapse;"> <tr><td>Inspection Date</td><td>22-May-25</td></tr> <tr><td>Work Order #</td><td>ICE-23894</td></tr> <tr><td>PO#</td><td>-</td></tr> <tr><td>Test Method</td><td>ASTM E709</td></tr> <tr><td>Inspection Type</td><td>Certification</td></tr> <tr><td>Location</td><td>TeKh - Yard</td></tr> <tr><td>Procedure</td><td>MT NDT-0000 Section 4</td></tr> <tr><td>Acceptance Standard</td><td>CSA W59/API 8C/ICON Spec</td></tr> <tr><td>Yoke Manufacturer</td><td>Magswitch</td></tr> <tr><td>Yoke Calibration</td><td>22-May-25</td></tr> <tr><td>Blacklight Manufacturer</td><td>Labino</td></tr> <tr><td>Blacklight Calibration</td><td>22-May-25</td></tr> <tr><td>Lightmeter Manufacturer</td><td>Spectroline</td></tr> <tr><td>Lightmeter Calibration</td><td>21-Jun-24</td></tr> <tr><td>Magnetic Particles</td><td>Powder</td></tr> <tr><td>Material Temp (Celsius)</td><td>(5°C to 70°C)</td></tr> </table>	Inspection Date	22-May-25	Work Order #	ICE-23894	PO#	-	Test Method	ASTM E709	Inspection Type	Certification	Location	TeKh - Yard	Procedure	MT NDT-0000 Section 4	Acceptance Standard	CSA W59/API 8C/ICON Spec	Yoke Manufacturer	Magswitch	Yoke Calibration	22-May-25	Blacklight Manufacturer	Labino	Blacklight Calibration	22-May-25	Lightmeter Manufacturer	Spectroline	Lightmeter Calibration	21-Jun-24	Magnetic Particles	Powder	Material Temp (Celsius)	(5°C to 70°C)
Customer	<b>TEKH GROUP INC.</b>																																																						
Branch	-																																																						
Equipment Type	Side Boom																																																						
Make	Caterpillar																																																						
Model	D6C																																																						
Capacity	Refer to OEM Capacity																																																						
Size	-																																																						
Other	-																																																						
OEM S/N	90B596																																																						
Customer ID	-																																																						
Rig/Unit:	72-634																																																						
Inspection Date	22-May-25																																																						
Work Order #	ICE-23894																																																						
PO#	-																																																						
Test Method	ASTM E709																																																						
Inspection Type	Certification																																																						
Location	TeKh - Yard																																																						
Procedure	MT NDT-0000 Section 4																																																						
Acceptance Standard	CSA W59/API 8C/ICON Spec																																																						
Yoke Manufacturer	Magswitch																																																						
Yoke Calibration	22-May-25																																																						
Blacklight Manufacturer	Labino																																																						
Blacklight Calibration	22-May-25																																																						
Lightmeter Manufacturer	Spectroline																																																						
Lightmeter Calibration	21-Jun-24																																																						
Magnetic Particles	Powder																																																						
Material Temp (Celsius)	(5°C to 70°C)																																																						

EQUIPMENT				TEST MEDIUM		TECHNIQUE			
Hand Yoke	<input type="checkbox"/>	No. N4846	Alloy Analyzer	<input type="checkbox"/>	No.	<input type="checkbox"/>	<u>MPI</u>	<input type="checkbox"/>	<u>LPI</u>
Perm Magnet	<input checked="" type="checkbox"/>	No. 31820120287	Hardness Tester	<input type="checkbox"/>	No.	<input checked="" type="checkbox"/>	AC	<input type="checkbox"/>	Water Washable
Blacklight	<input type="checkbox"/>	No. 35217	UT Detector	<input type="checkbox"/>	No.	<input type="checkbox"/>	DC	<input type="checkbox"/>	Post Emulsified
Coil	<input type="checkbox"/>	No. C306	UT Probe	<input type="checkbox"/>	No.	<input type="checkbox"/>	Continuous	<input checked="" type="checkbox"/>	Solvent Removable
Gauss Meter	<input type="checkbox"/>	No.	Lightmeter	<input type="checkbox"/>	No. 2181659	<input type="checkbox"/>	Residual	<input type="checkbox"/>	Dwell Time (min)
Surface Condition	Painted								
UTX	<input type="checkbox"/>			<input type="checkbox"/>			<input type="checkbox"/>	Develop Time (min)	

**EXAMINATION:**  
 Magnetic Particle and Visual Examination was performed on 100% of the accessible areas on the items listed above.

**PHOTO/NOTES:**

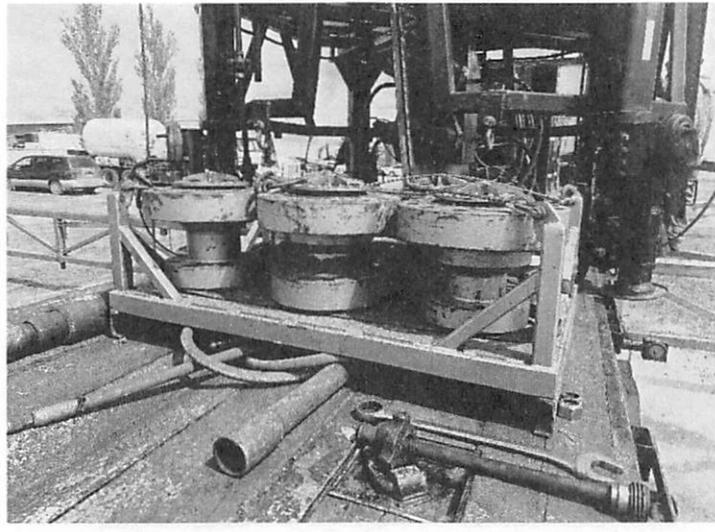

**RESULTS:**  
 No relevant indications were noted at the time of inspection.

The results of inspected items reported by the company to the customer represent good faith opinions only and are not to be considered warranties or guarantees of quality, classification or usability of items inspected.

Technician  <b>BRENT WOODS</b> MT2/XF2/DS1 CGSB Reg.# 18438 SNT-TC-1A Reg.# 18438 DS1# DS1_118119022023	Signature  	Assistant  <b>DARRELL SPENCE</b>	Client Rep/Signature			
Document Information						
Doc#	Rev.	Rev. Date	Doc Name	Reviewer	Approver	Appr. Date
NDT-0401-00	7	2023-11-08	NDT Report (General)	BW	RE	2023-11-08



**ANNUAL INSPECTION - Sideboom Tractor and Boom**

DS-0958

Hours:	12183
Date:	May 22, 2025

VT=VISUAL  
MT=MAG PARTICLE

**SIDEBOOM TRACTOR**

	VT	MT	OK	N/A	NOTES
Boom to Frame Mounting	X	X	X		
Boom Mount Pins and Retainers	X		X		
Counter Weight Mounting/Structure	X	X	X		
Counter Weight Track/Cylinders	X		X		
ROPS Structure				X	

ROPS S/N:	-
-----------	---

**SIDEBOOM STICK**

	VT	MT	OK	N/A	NOTES
Boom Sections (Welds)	X	X	X		
Boom Sections (Camber/Twist Sweep)	X		X		
Boom Hinge				X	
Boom Pins/Hardware/Retainers	X		X		
Boom Cathead/Sheave/Pin	X	X	X		

**SIDEBOOM STICK**

Make:	CATERPILLAR
Model:	20' A-FRAME
S/N:	72-634
Capacity:	-

**JIB ATTACHMENT**

	VT	MT	OK	N/A	NOTES
Jib Boom Section (Welds)				X	
Jib Boom Section (Camber/Twist/Sweep)				X	
Jib Pins/Hardware/Retainers				X	

**JIB ATTACHMENT**

Make:	-
Model:	-
S/N:	-

**MAIN LINE BLOCK/RIGGING**

	VT	MT	OK	N/A	NOTES
Block/Sheave Condition	X		X		
Hook/Latch Condition	X	X	X		
Hardware/Pins/Retainers	X		X		
Cable/Rigging/Hardware	X		X		
Winch Mounts/Fasteners/Structure	X	X	X		

**BLOCK/HOOK**

Make:	-
Model:	-
S/N:	-
Capacity:	-

**HOIST LINE BLOCK/RIGGING**

	VT	MT	OK	N/A	NOTES
Block/Sheave Condition	X		X		
Hook/Latch Condition					
Hardware/Pins/Retainers	X		X		
Cable/Rigging/Hardware	X		X		
Winch Mounts/Fasteners/Structure	X	X	X		

**BLOCK/HOOK**

Make:	-
Model:	-
S/N:	-
Capacity:	-

**GENERAL**

	VT	MT	OK	N/A	NOTES
Capacity and Controls Clearly Marked	X				
Anti-Two Block Device				X	
General Condition/Corrosion	X		X		
Load Indicator				X	
Load Chart	X				

Comments and Recommendations

**Document Information**

Doc#	Rev.	Rev. Date	Doc Name	Reviewer	Approver	Appr. Date
NDT-0510-00	8	2024-11-20	Annual Inspection Checklists	BW	RE	2024-11-20
