



HOIST LTD.

780 818-5664
certifiedhoist.ca

10280 276 Street
Acheson, AB T7X 6A5

Technical Field Report

Lifting Technologies Incorporated

28527 Acheson Rd.
Acheson, AB T7X 6A8

Attention: Wes Bartel

Type of Work: Structural Inspection of Manbasket and Spreader Bar

Equipment:

Man Basket Model: See Below Serial: See Below Unit: See Below
Mfg. Year: See Below
Manufacturer: LTI
Location: MSR Quonset

Our File: 24-E090
Inspection Date: 09/25/2024
P.O.:



Visual examinations and magnetic particle inspections were performed on the above-described equipment. The specific items examined and our inspection findings were as follows:

NID: No Indications Dectected

1. Unit: MR-MB33BJ, SN:MR-MB44BJ, MN:MR-MB44V3
Center Pole
Top Rail
Pinch Rail
Mid Rail
Frame
Floor/Base
Test Weight
Lift Lugs (x4)
2. LTI Spreader Bar Capacity: 25 ton, Unit: MR-1219AJ - NID
Model: MR-1219, Serial: MR-1219AJ, Manufacture Year: 2012

Inspected by:

Formal Report to Follow

J. Landry


L. Nguy P. Eng



28397 Acheson Road
Acheson, AB
T7X 6A8
780 818 5664

Test Certificate

Customer:	LTI	Certificate No.	2410001-01C
Description:	1/2" Wire Rope Rigging Bridle(Test:Legs)(Red:Legs 1&2, Green:Legs 3&4, Purple:Leg 5)		
Date:	2024-10-04	Test Type:	90 Deg.
Rigging WLL:	5000 @ 60 Deg. LBS	Cycle Test Time (sec)	20
Length:	10&4 FT	Number of Legs:	5
Proof Percentage:	125 %	Manufacturer:	N/A
Test Load:	6250 LBS	Tag:	MR-MBR-15
Event Number:	3075	Serial:	MR-MBR-15

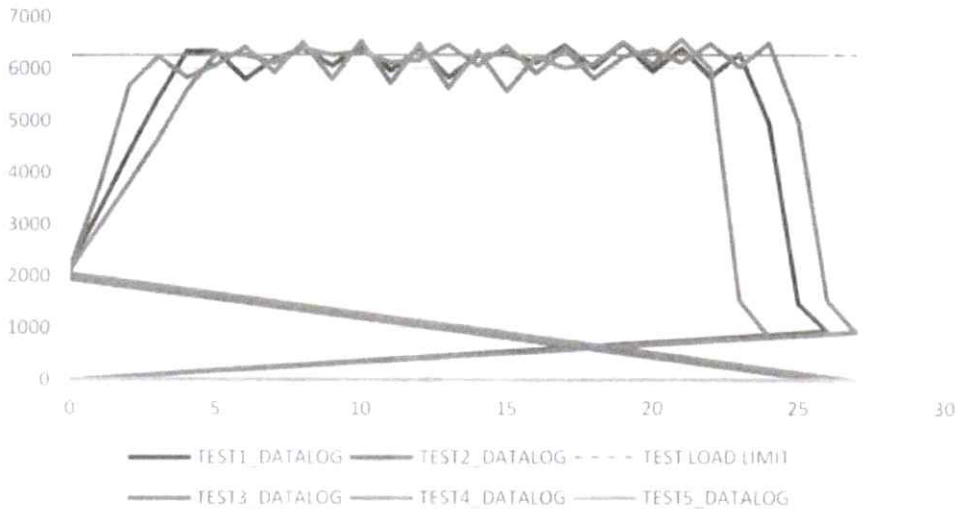

Test Bed Serial: 6314
Last Calibrated: 21-Jun-23



Conducted by: HOIST LTD.

Dean Medley

TEST RESULTS:

ACCEPTABLE
 NOT ACCEPTABLE

Certified Hoist hereby certifies that pull-testing the product described herein has taken place and obtained the results set out above. The testing performed by Certified Hoist reflects the performance of the products as of the date of testing and under the conditions that the testing occurred. It is the user's responsibility to ensure that the products meet the requirements of ASME B30.9 and Part 21 of OH&S 2020 Code, and that the product is inspected and used in accordance with all applicable laws, regulations, and requirements.




HOIST LTD.

28397 Acheson Road
Acheson, AB
T7X 6A8
780 818 5664

Test Certificate

Customer:	LTI	Certificate No.	2410001-01B
Description:	1/2" Wire Rope Rigging Bridle(Test:Secondary D-Rings)		
Date:	2024-10-04	Test Type:	90 Deg.
Rigging WLL:	5000 LBS	Cycle Test Time (sec)	20
Length:	1 FT	Number of Legs:	2
Proof Percentage:	125 %	Manufacturer:	N/A
Test Load:	6250 LBS	Tag:	MR-MBR-15
Event Number:	3074	Serial:	MR-MBR-15

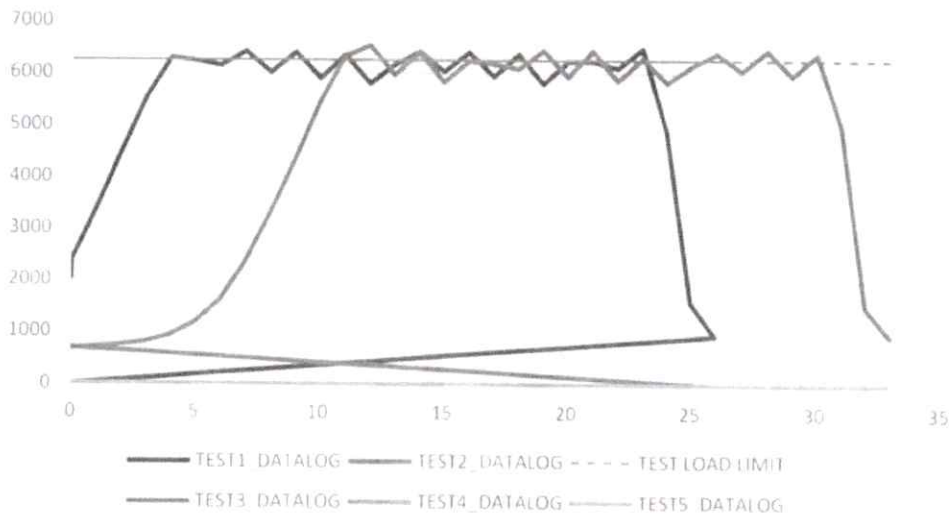

Test Bed Serial: 6314
Last Calibrated: 21-Jun-23



Conducted by: HOIST LTD.

Dean Medley

Dean Medley

TEST RESULTS:

ACCEPTABLE
 NOT ACCEPTABLE


Certified Hoist hereby certifies that pull-testing the product described herein has taken place and obtained the results set out above. The testing performed by Certified Hoist reflects the performance of the products as of the date of testing and under the conditions that the testing occurred. It is the user's responsibility to ensure that the products meet the requirements of ASME B30.9 and Part 21 of OH&S 2020 Code, and that the product is inspected and used in accordance with all applicable laws, regulations, and requirements.



28397 Achescn Road
Acheson, AB
T7X 6A8
780 818 5664

Test Certificate

Customer:	LTI	Certificate No.	2410001-01A
Description:	1/2" Wire Rope Rigging Bridle(Test:Main D-Ring)		
Date:	2024-10-04	Test Type:	90 Deg.
Rigging WLL:	5000 LBS	Cycle Test Time (sec)	20
Length:	1 FT	Number of Legs:	1
Proof Percentage:	125 %	Manufacturer:	N/A
Test Load:	6250 LBS	Tag:	MR-MBR-15
Event Number:	3073	Serial:	MR-MBR-15

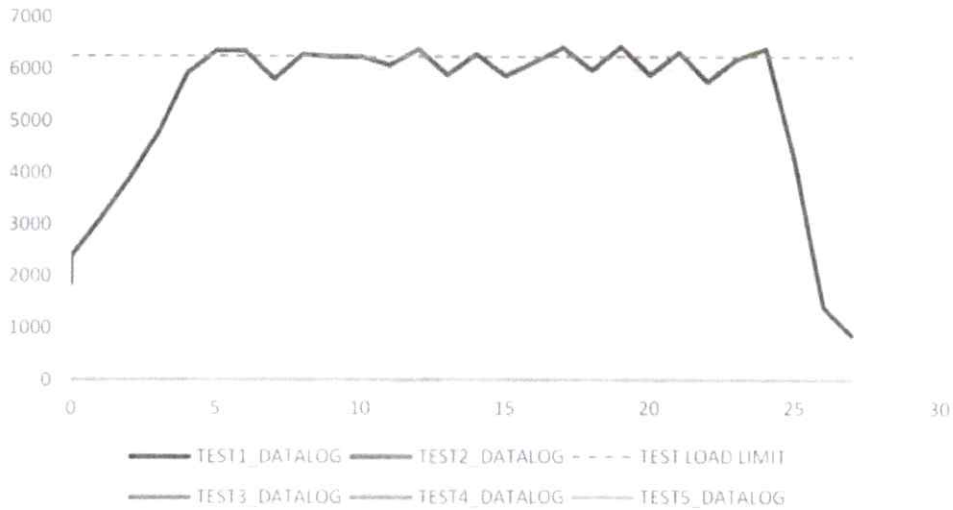

Test Bed Serial: 6314
Last Calibrated: 21-Jun-23



Conducted by: HOIST LTD.

Dean Medley

TEST RESULTS:

ACCEPTABLE
 NOT ACCEPTABLE

Certified Hoist hereby certifies that pull-testing the product described herein has taken place and obtained the results set out above. The testing performed by Certified Hoist reflects the performance of the products as of the date of testing and under the conditions that the testing occurred. It is the user's responsibility to ensure that the products meet the requirements of ASME B30.9 and Part 21 of OH&S 2020 Code, and that the product is inspected and used in accordance with all applicable laws, regulations, and requirements.




HOIST LTD.

28397 Acheson Road
Acheson, AB
T7X 6A8
780 818 5664

Test Certificate

Customer:	LTI	Certificate No.	2410001-02
Description:	7/16"x4' Wire Rope Sling		
Date:	2024-10-04	Test Type:	90 Deg.
Rigging WLL:	3800 LBS	Cycle Test Time (sec)	20
Length:	4 FT	Number of Legs:	1
Proof Percentage:	125 %	Manufacturer:	supersling
Test Load:	4750 LBS	Tag:	109778-2
Event Number:	3076	Serial:	109778-2

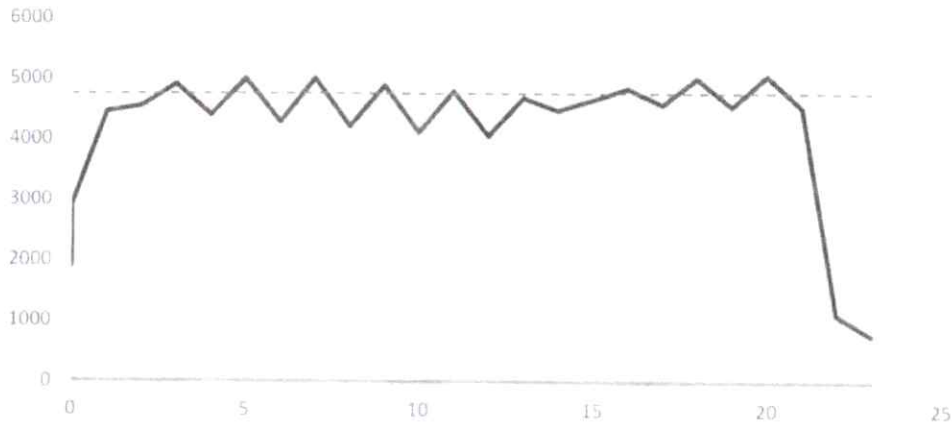

— TEST1_DATALOG — TEST2_DATALOG - - - - TEST LOAD LIMIT
 — TEST3_DATALOG — TEST4_DATALOG — TEST5_DATALOG

Test Bed Serial: 6314
Last Calibrated: 21-Jun-23



Conducted by: **HOIST LTD.**

Dean Medley

TEST RESULTS:

ACCEPTABLE
 NOT ACCEPTABLE

Certified Hoist hereby certifies that pull-testing the product described herein has taken place and obtained the results set out above. The testing performed by Certified Hoist reflects the performance of the products as of the date of testing and under the conditions that the testing occurred. It is the user's responsibility to ensure that the products meet the requirements of ASME B30.9 and Part 21 of OH&S 2020 Code, and that the product is inspected and used in accordance with all applicable laws, regulations, and requirements.



Myshak Sales & Rentals Ltd.
 28527 Acheson Rd
 Acheson, AB T7X 6A8
 Phone No.: 780-960-9255

CONTRACT

Contract Number: RA021906
 Contract Date: 10/4/2024
 Page: 1 of 1

P05-12

Bill
 To: LOON RIVER TRUCKING LTD.
 Sherisse Kazlauskas
 BOX 189
 RED EARTH CREEK, AB T0G 1X0

Ship
 To: LOON RIVER TRUCKING LTD.
 TONY
 BOX 189
 RED EARTH CREEK, AB T0G 1X0

Customer ID L0001
 SalesPerson Wes Bartel
 Cust. Job #
 AFE No.

Terms Due Upon Receipt
 Tax Registration 89711 7347
 Cust. Reference
 Invoiced On

External Document
 Shipment Method
 LSD Location

Type	Contact Name	Phone No.	Mobile Phone No.	E-Mail
Ship-to	TONY	780-649-1111		

General Comments: ANNUAL MPI & PULL TEST INSPECTION ON CUSTOMER OWNED UNITS.

Description	Dates	Qty	Unit Price	Total Price
MPI INSPECTION - CUSTOMER OWNED 4'X4' MAN BASKET	10/04/24	1 Each		
MPI INSPECTION - CUSTOMER OWNED 12'-19' SPREADER BAR	10/04/24	1 Each		
PULL TEST INSPECTION ON CUSTOMER OWNED BRIDLE	10/04/24	1 Each		

Customer accepts and acknowledges the terms & conditions listed on the back of this agreement. Equipment accepted and equipped as per mechanical outgoing report. Customer is responsible for safe operation, qualified operators, general upkeep and maintenance.

Above Equipment to be Insured by the Lessee. *** DO NOT PAY, THIS IS A CONTRACT ONLY. INVOICE TO FOLLOW ***

Amount Subject to Sales Tax
 Amount Exempt from Sales Tax 0.00

Subtotal:
 Invoice Discount:
 Total Tax:

Total:

Printed Name

Signature

Date
